LAB 2

Agile Backlog and Sprint Simulation

Inter-City Freight Load Matching Marketplace

Name	Atharv Kulkarni
SRN	PES2UG24CS092
Project Board	ICFLMM board
Sprint	ICFLMM Sprint 1
Sprint Duration	2 weeks
Sprint Scope	24 story points

Submission contents: Epics and backlog, story-point assignments, Sprint 1 planning, Active Sprint board, Burndown Chart, and reflection answers.

1. Epics and Agile Backlog


The Jira backlog was organized into four functional epics. The 10 user stories below represent the functional and non-functional requirements from Lab 1 and were estimated using relative story points.

Epic / Area	Story ID	User Story	Points
Freight & Capacity Management	US-01	Post Freight Load	3
Freight & Capacity Management	US-02	Publish Transport Capacity	3
Load Matching	US-03	View Matching Opportunities	5
Load Matching	US-04	Check Match Eligibility	3
Booking Management	US-05	Request Freight Booking	5
Booking Management	US-06	Accept / Reject Booking	3
Booking Management	US-07	View Booking Status	2

Marketplace Administration	US-08	Manage Users and Listings	3
Non-functional requirement	US-09	Meet Matching Response-Time Requirement	3
Non-functional requirement	US-10	Secure Booking Management	5

Total backlog: 35 story points across 10 work items.

Requirement mapping: US-01/US-02 map to FR-001/FR-002; US-03/US-04 map to FR-003 and match eligibility; US-05/US-06/US-07 map to FR-004/FR-005 and booking status; US-08 maps to UC-07 administration; US-09 and US-10 represent NFR-001/NFR-002.

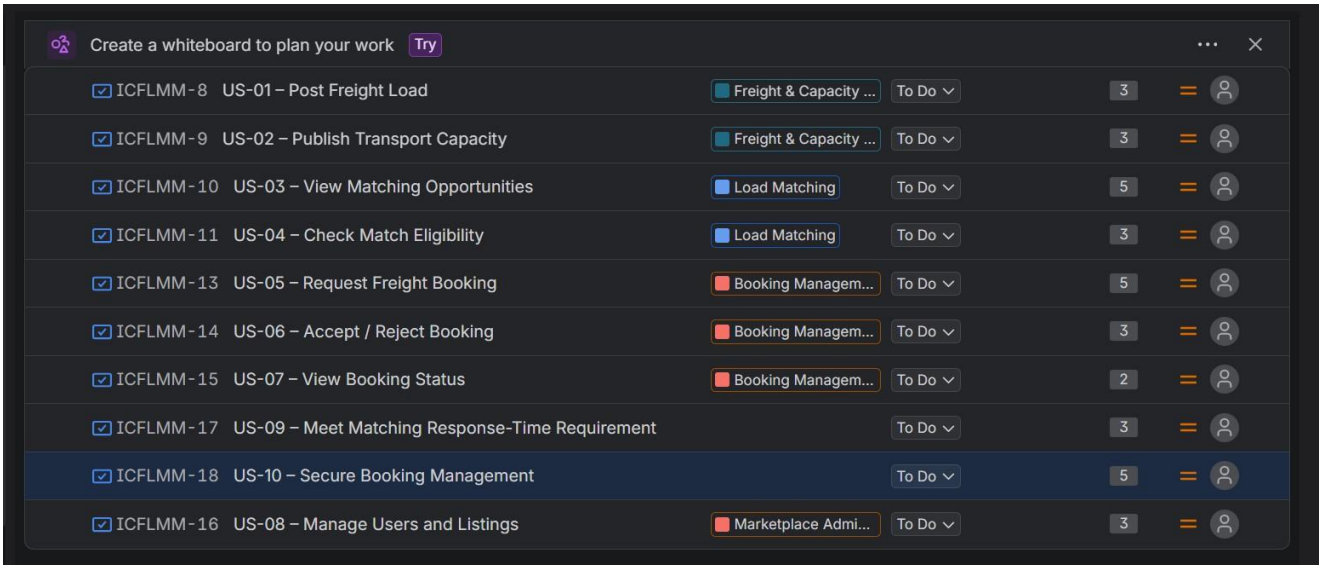

Jira List view showing the created user stories, their epic assignments, statuses, and story-point estimates.


2. Story-Point Assignments and Sprint 1 Planning

Story points were assigned by relative complexity and effort. The core end-to-end workflow was selected for Sprint 1, giving a sprint scope of 24 points.

Sprint 1 Story	Points	Status at Planning
US-01 - Post Freight Load	3	To Do
US-02 - Publish Transport Capacity	3	To Do
US-03 - View Matching Opportunities	5	To Do
US-04 - Check Match Eligibility	3	To Do
US-05 - Request Freight Booking	5	To Do

US-06 - Accept / Reject Booking	3	To Do
US-07 - View Booking Status	2	To Do


Sprint 1 scope: 7 work items, 24 story points. The remaining backlog items US-08, US-09 and US-10 were left outside Sprint 1.

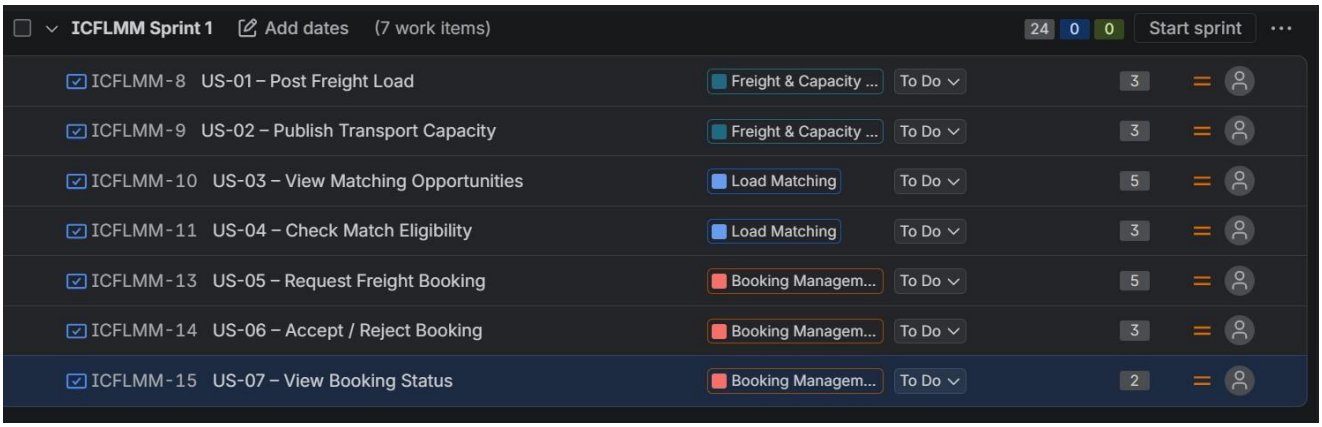

Jira backlog showing ICFLMM Sprint 1 with 7 work items and 24 story points before the sprint was started.

3. Active Sprint View - Sprint Simulation

The sprint was started as a two-week simulation. At the recorded progress point, two stories were completed, one was in progress, and four remained to do.

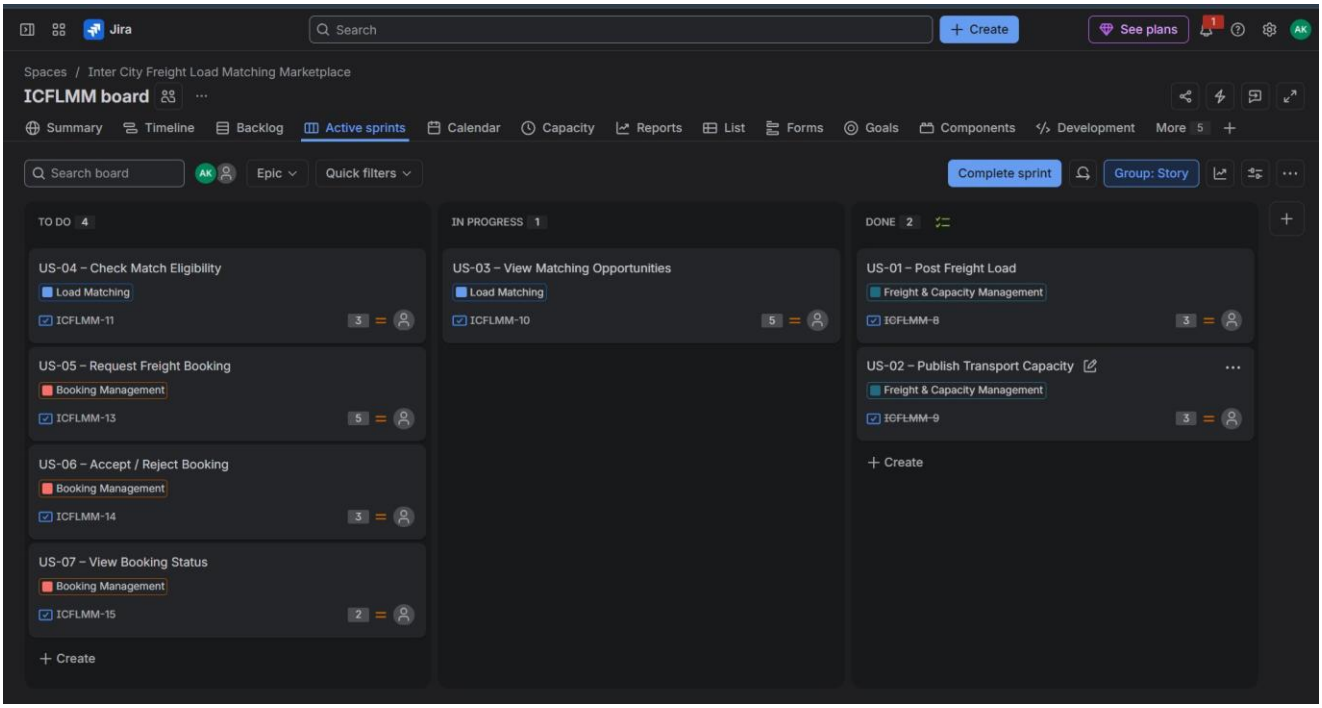

Column	Stories	Points
Done	US-01, US-02	6
In Progress	US-03	5
To Do	US-04, US-05, US-06, US-07	13
Sprint scope	7 stories	24


At this point, 6 of 24 sprint points had been completed, leaving 18 points remaining.

4. Burndown Chart

The Jira Burndown Chart uses Story Points as the estimation statistic and shows the sprint guideline together with the recorded remaining work.



Observed sprint state: starting scope 24 points; 6 points completed; 18 points remaining. The chart therefore provides evidence of a 25% completion point during the simulation.

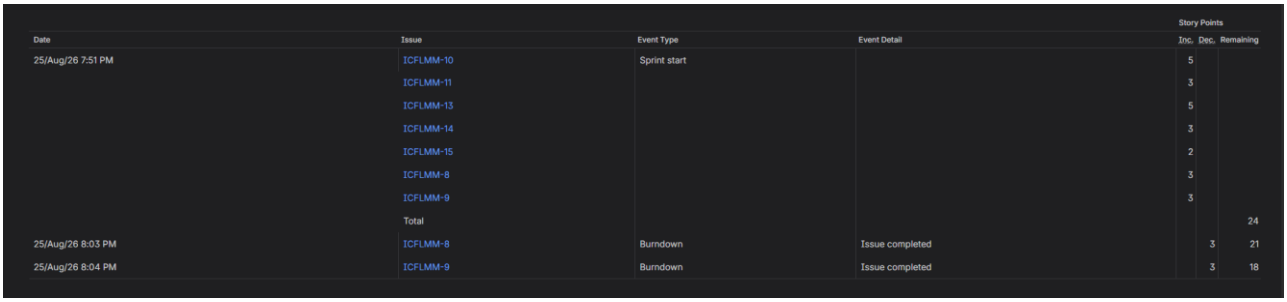

				Story Points		
Date	Issue	Event Type	Event Detail	Inc.	Dec.	Remaining
25/Aug/26 7:51 PM	ICFLMM-10	Sprint start		5		
	ICFLMM-11			3		
	ICFLMM-13			5		
	ICFLMM-14			3		
	ICFLMM-15			2		
	ICFLMM-8			3		
	ICFLMM-9			3		
	Total					24
25/Aug/26 8:03 PM	ICFLMM-8	Burndown	Issue completed		3	21
25/Aug/26 8:04 PM	ICFLMM-9	Burndown	Issue completed		3	18

5. Reflection Questions

1. Did your estimations reflect the actual effort?

The story-point estimates provided a reasonable relative view of effort. More complex functions such as View Matching Opportunities and Request Freight Booking were assigned 5 points, while simpler work such as View Booking Status was assigned 2 points. Because this was a simulated sprint and no real implementation work was performed, the estimates cannot be compared with actual development effort.

2. Was your backlog well-prioritized?

Yes. The backlog was organized around the main marketplace workflow. The core functions were prioritized first: posting freight, publishing transport capacity, checking eligibility, finding matches, requesting bookings, accepting or rejecting bookings, and viewing booking status. Administrative and non-functional work was kept outside the first sprint.

3. How did your simulated sprint align with your plan?

The sprint aligned with the plan by selecting the seven core stories that form the main end-to-end workflow. Sprint 1 contained 24 story points. During the simulation, two stories worth 6 points were completed, one 5-point story was in progress, and four stories remained in To Do. The sprint therefore reflected the planned scope while making remaining work visible.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed an initial sprint scope of 24 story points and 18 points remaining after 6 points of work were completed. This means 25% of the planned sprint effort had been completed at the recorded point. The chart also showed that a substantial amount of work remained, indicating that continued progress would be required to reach the sprint goal. Because the exercise was a simulation, this represents simulated capacity rather than measured team velocity.

Submission summary

This document contains the Jira evidence for Epics and backlog, story-point estimation, Sprint 1 planning, Active Sprint progress, Burndown Chart, and the four required reflection answers.
